



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2, 2020	Qtr 3, 2020	Qtr 4, 2020	Qtr 1, 2021	Qtr 2, 2021	Qtr 3, 2021	Qtr 4, 2021	Qtr 1, 2022	Qtr 2, 2022	Qtr 3, 2022
								May Jun	Jul Aug Sep	Oct Nov Dec	Jan Feb Mar	Apr May Jun	Jul Aug Sep	Oct Nov Dec	Jan Feb Mar	Apr May Jun	Jul Aug Sep
1		<b>Pedestrian Crossing adjacent to 15 Church Street, Brighton</b>	<b>543.5 days</b>	<b>Thu 18/06/20</b>	<b>Tue 19/07/22</b>												
2		<b>Concept Stage</b>	<b>0 days</b>	<b>Thu 18/06/20</b>	<b>Thu 18/06/20</b>												
3		Project Concept Approved	0 days	Thu 18/06/20	Thu 18/06/20												
4		<b>Plan Stage</b>	<b>168 days</b>	<b>Thu 18/06/20</b>	<b>Mon 08/02/21</b>												
5		Complete Due Dilligence check & Risk	1 wk	Thu 18/06/20	Wed 24/06/20	3											
6		Functional Design	60 days	Thu 25/06/20	Wed 16/09/20												
7		DOT Approval (in Principle)	2 wks	Wed 01/07/20	Tue 14/07/20	5											
8		Request for design, survey, service depthing, specification, BOQ & cost estimate quote	1 day	Thu 25/06/20	Thu 25/06/20	5											
9		Receive quote	1 day	Tue 07/07/20	Tue 07/07/20	8FS+7 days											
10		Award survey & design contract	1 day	Wed 15/07/20	Wed 15/07/20	9FS+2 days,7											
11		Complete survey	2 wks	Thu 16/07/20	Wed 29/07/20	10											
12		Underground Services Proving	1.5 wks	Thu 30/07/20	Mon 10/08/20	11											
13		Produce Functional Design	1.5 wks	Thu 30/07/20	Mon 10/08/20	11											
14		Approval of Functional Design	1 day	Mon 24/08/20	Tue 25/08/20	13FS+2 wks,7											
15		Request for Quote - RSA	1 day	Tue 25/08/20	Wed 26/08/20	14											
16		Receive quote	0 days	Wed 02/09/20	Wed 02/09/20	15FS+1 wk											
17		Award RSA Contract	1 day	Fri 04/09/20	Mon 07/09/20	16FS+2 days											
18		Complete RSA	1.5 wks	Mon 07/09/20	Wed 16/09/20	17											
19		<b>Design Development</b>	<b>100 days</b>	<b>Thu 17/09/20</b>	<b>Wed 03/02/21</b>												
20		Review of Design based on RSA Recommednation	1 wk	Thu 17/09/20	Wed 23/09/20	18											
21		Complete Preliminary Design (Civil+Electrical)	4 wks	Thu 17/09/20	Wed 14/10/20	20SS											
22		Complete Detail Civil Design	2 wks	Thu 15/10/20	Wed 28/10/20	20,21											
23		Approval Process with DOT	4 wks	Thu 29/10/20	Wed 25/11/20	22											

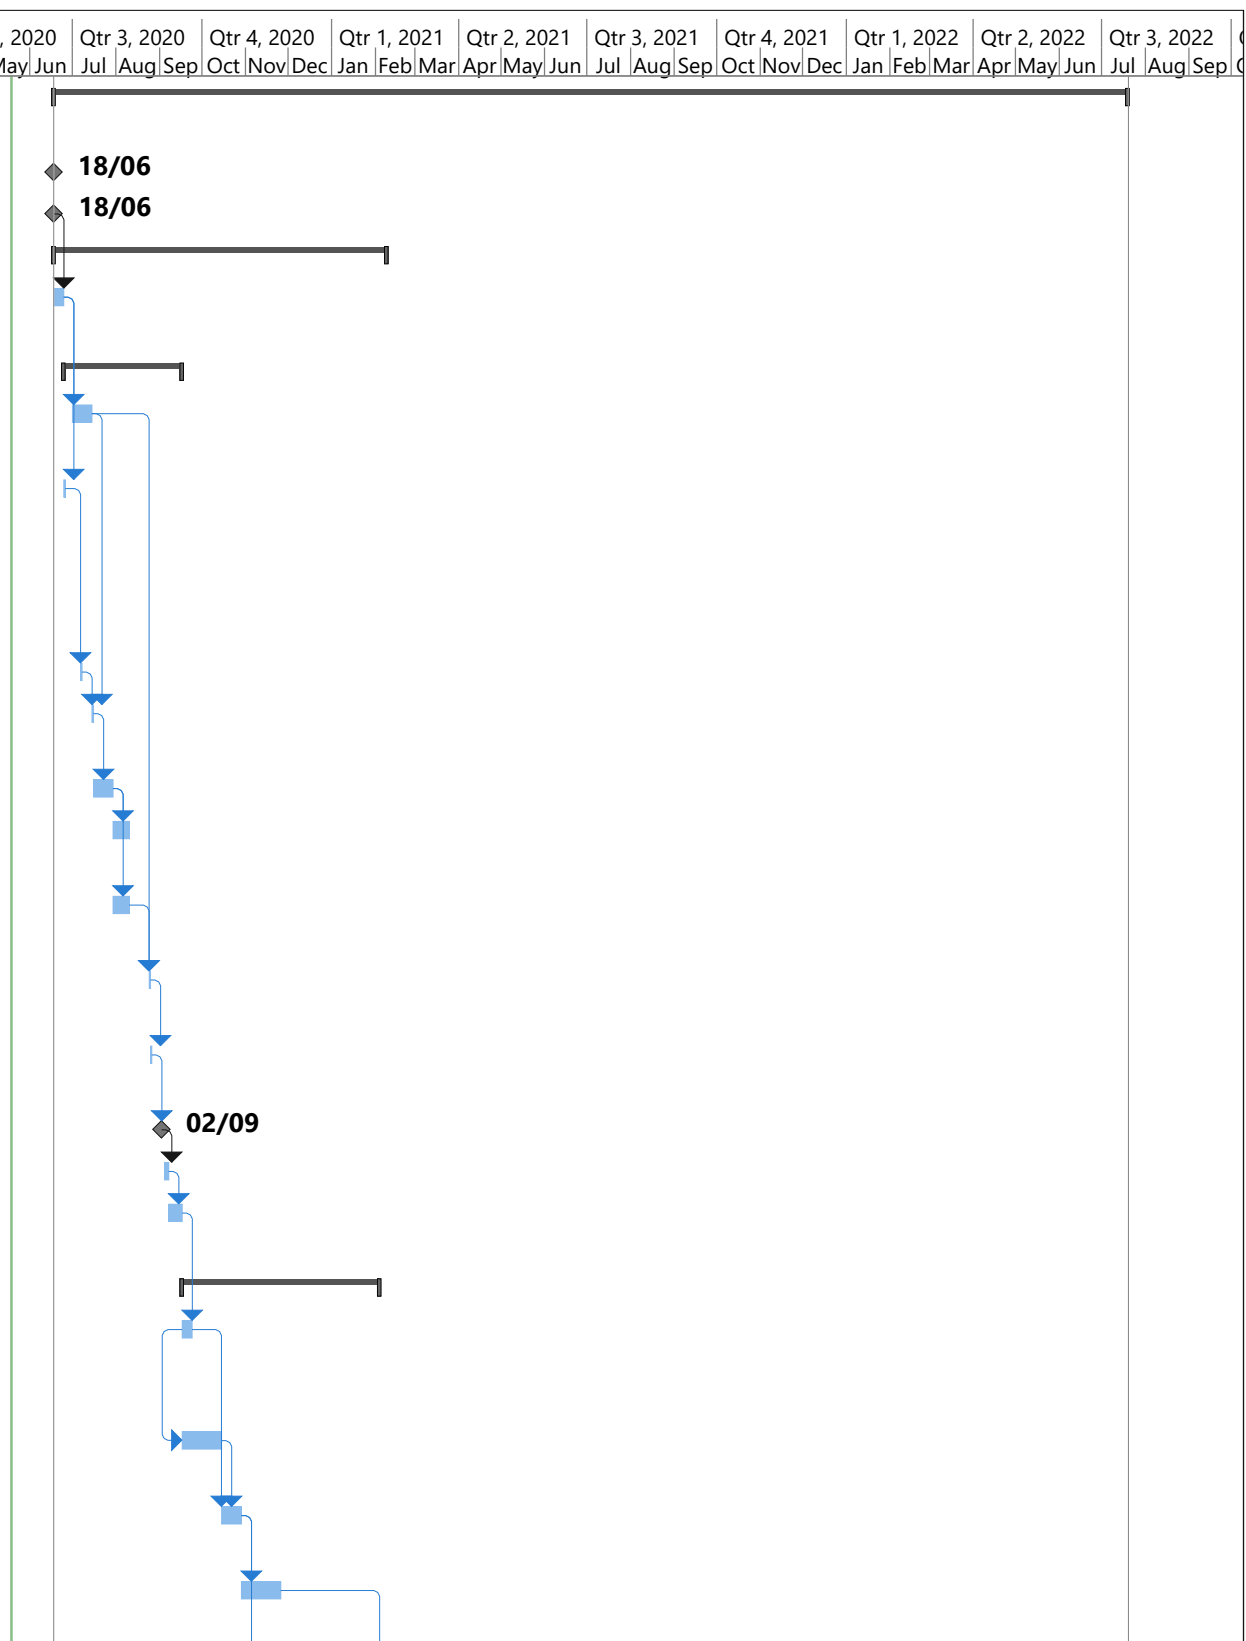

Project: Active Transport Facility  
Date: Tue 19/05/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2, 2020	Qtr 3, 2020	Qtr 4, 2020	Qtr 1, 2021	Qtr 2, 2021	Qtr 3, 2021	Qtr 4, 2021	Qtr 1, 2022	Qtr 2, 2022	Qtr 3, 2022
								May Jun	Jul Aug Sep	Oct Nov Dec	Jan Feb Mar	Apr May Jun	Jul Aug Sep	Oct Nov Dec	Jan Feb Mar	Apr May Jun	Jul Aug Sep
24		Approval Process with Power Authority including sourcing confirmed point of supply	14 wks	Thu 29/10/20	Wed 03/02/21	22											
25		Business Case Approved	0 days	Mon 08/02/21	Mon 08/02/21	24FS+3 days											
26		<b>Delivery Stage</b>	<b>108.5 days</b>	<b>Thu 04/02/21</b>	<b>Tue 06/07/21</b>												
27		Construction Contract Documentation	1 wk	Thu 04/02/21	Wed 10/02/21	23,24											
28		Tender	31.5 days	Thu 11/02/21	Mon 29/03/21												
29		Release RFT for construction	0 days	Thu 11/02/21	Thu 11/02/21	27FS+1 day											
30		Receive RFT for construction	1 day	Tue 09/03/21	Tue 09/03/21	29FS+17 days											
31		Evaluate tender and recommend	2.5 wks	Wed 10/03/21	Fri 26/03/21	30											
32		Contract Award	1 day	Fri 26/03/21	Mon 29/03/21	31											
33		Works	51 days	Mon 26/04/21	Tue 06/07/21												
34		Commence construction	1 day	Mon 26/04/21	Tue 27/04/21	32FS+4 wks											
35		Construction work including point of supply for the flashing lights and controller	10 wks	Tue 27/04/21	Tue 06/07/21	34											
36		Project Completed	0 days	Tue 06/07/21	Tue 06/07/21	35											
37		<b>Close Stage</b>	<b>270 days</b>	<b>Tue 06/07/21</b>	<b>Tue 19/07/22</b>												
38		Project Close	2 wks	Tue 06/07/21	Tue 20/07/21	36											
39		Defects Liability Period	52 wks	Tue 20/07/21	Tue 19/07/22	38											
40		Project Closed	0 days	Tue 19/07/22	Tue 19/07/22	39											

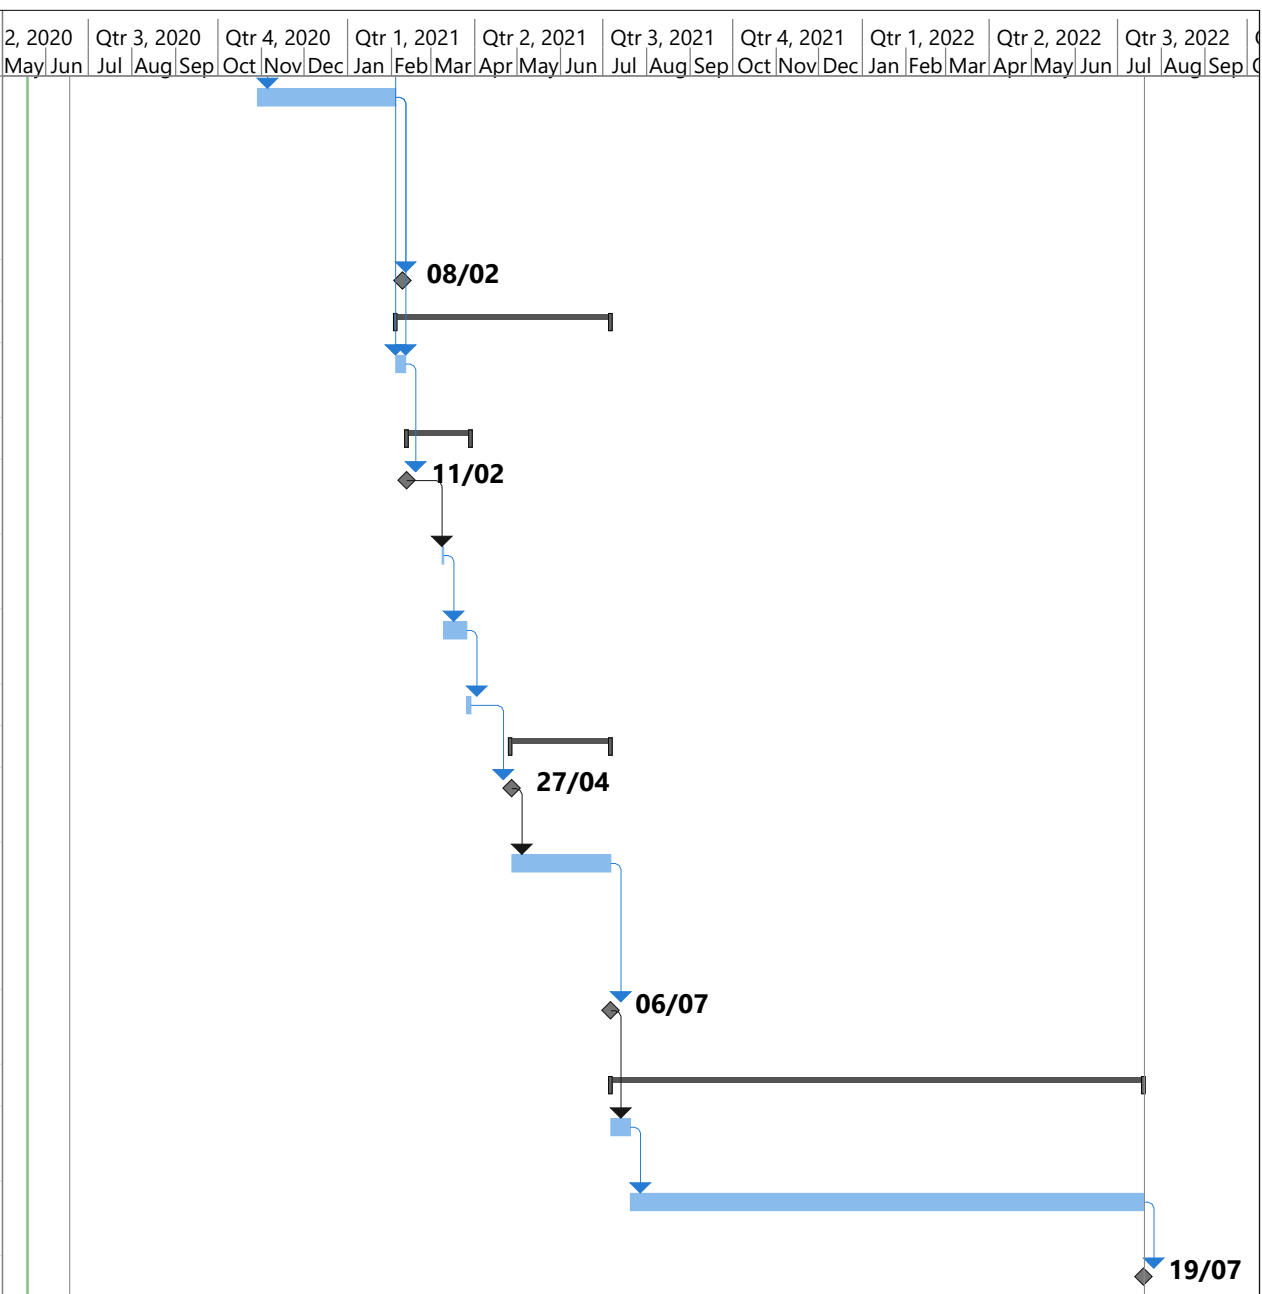

Project: Active Transport Facility  
Date: Tue 19/05/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
